




# MONTEZUMA - CORTEZ HIGH SCHOOL



## Weekly Report July 03, 2015

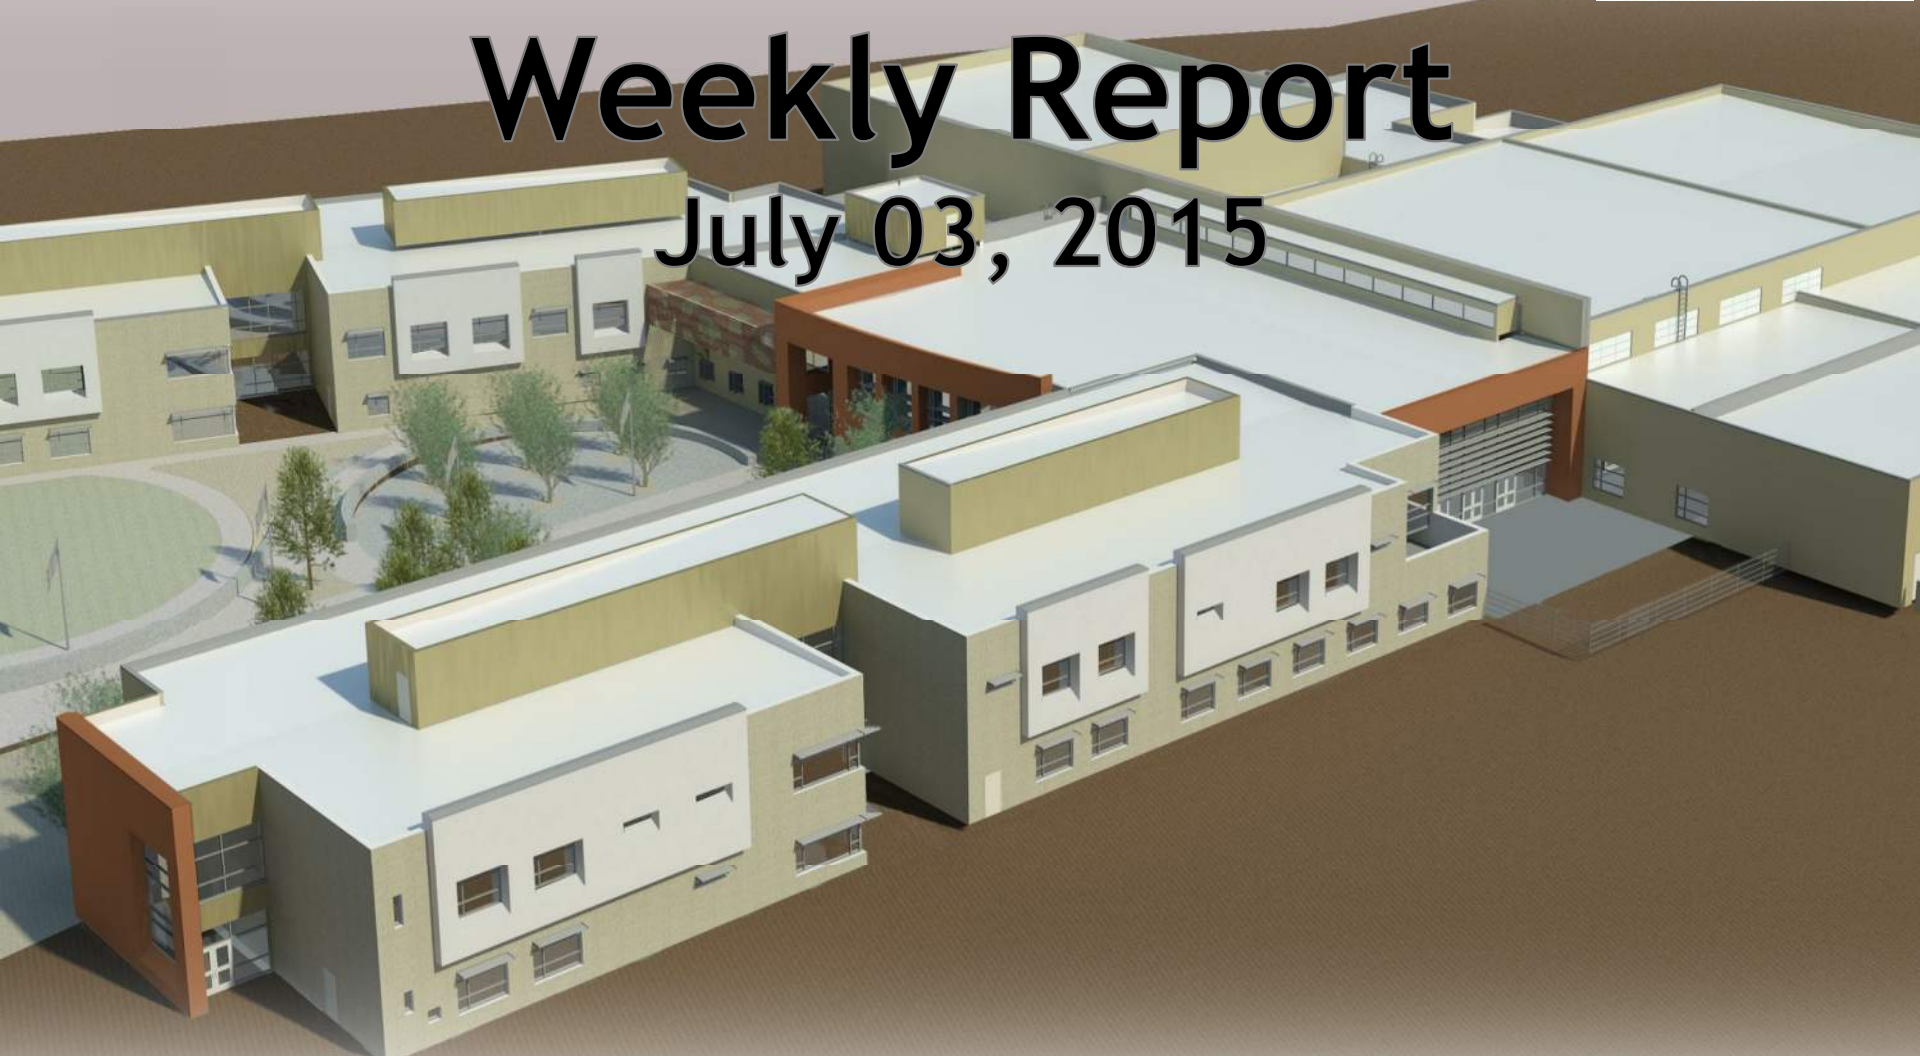

## 3-Week Look Ahead at Construction Schedule

- Roof ladders in all areas will be completed.
- Work on Plaza modifications will be complete.
- Work will begin on Multipurpose Field No. 2.
- Installation of irrigation system throughout the site will be completed. All landscaping, planting and native seeding will be completed.
- Mechanical, plumbing and electrical trimout will be completed.
- Startup, testing and balancing of Heat Pumps, ERV's and Roof Top Units will be completed.
- Functional testing and commissioning will continue.
- Installation of Kitchen Equipment will be completed.
- Painting will be completed.
- Ceramic tile installation will be completed.
- Ceiling tile installation will be completed.
- Casework installation will be completed.
- Installation of marker boards, toilet partitions and toilet accessories will be completed.
- Installation of interior wood doors and hardware will be completed.
- Carpet and vinyl flooring will be completed throughout the building.
- Appliances will be installed.
- Window blinds and roller shades will be completed.
- All interior and exterior signage will be completed.

# Subcontractors On Site

- ADP Lemco (sports equipment installation)
- Advanced Concrete Solutions (site concrete/floor polishing)
- Advanced Contracting (toilet partitions and accessories)
- Ambassador Blind and Shutter
- American Fence Company
- Beaty Masonry
- Clark & Company (irrigation and landscaping)
- Cruzan Construction (rough carpentry, hollow metal doors & frames, wood doors)
- Denman Building Products (framing, insulation and drywall)
- Durango Plastering (air barrier and stucco)
- Dynamic Fire Protection
- El Paso Flooring (hardwood gymnasium floor)
- Four Corners Materials (asphalt paving)
- Goff Engineering (surveying)
- Horizon Environmental Services (native seeding)
- HVAC Solutions
- Nichols Electric
- OGB Architectural Millwork
- Reigles Mechanical (plumbing)
- Rio Grand Flooring (carpet, resilient vinyl flooring and wall tile)
- Sign Art (pylon sign)
- Solargreen Holdings (tubular skylights)
- Stagecraft Industries (stage rigging)
- Summit Sealants (air barrier and joint sealants)
- Sun Glass (windows, aluminum store fronts and curtain walls)
- ThyssenKrupp (elevator installation)
- Topline Installers (roofing and metal siding)
- Trautner Geotechnical (Owner's Testing Firm)
- WBS Coatings
- W. West Equipment (food service)

# Notable Onsite Activities This Week

- Continued installation of irrigation system and planting of trees and shrubs.
- Continued native grass seeding throughout the site.
- Continued work on the west Plaza concrete.
- Continued installing site furnishings.
- Continued window cleaning in the classroom wings and Commons.
- Continued painting throughout the building
- Continued installation of casework in Area G.
- Continued installation of ceiling grid and tile throughout Areas C & G.
- Continued electrical trimout in Areas F and G.
- Continued installation of door hardware throughout building.
- Continued installation of controls wiring in Areas C, F and G.
- Continued installation of plumbing fixtures in Areas C, F and G.
- Continued installation of kitchen equipment in kitchen and culinary arts.
- Continued testing and balancing heat pumps and ERV's.
- Continued punchlist corrections throughout the building.
- Continued final cleaning in the building.
- Owner began moving furniture into the building.

## Weekly Weather





# Furniture Staged in Commons



07/03/2015 12:18





Library Furnishings

07/03/2015 12:16





Courtyard Fencing

07/03/2015 12:25





Art Courtyard Wall

07/03/2015 12:28





07/03/2015 12:31

Landscaping in Main Courtyard
