




MONTEZUMA - CORTEZ HIGH SCHOOL



Weekly Report July 24, 2015

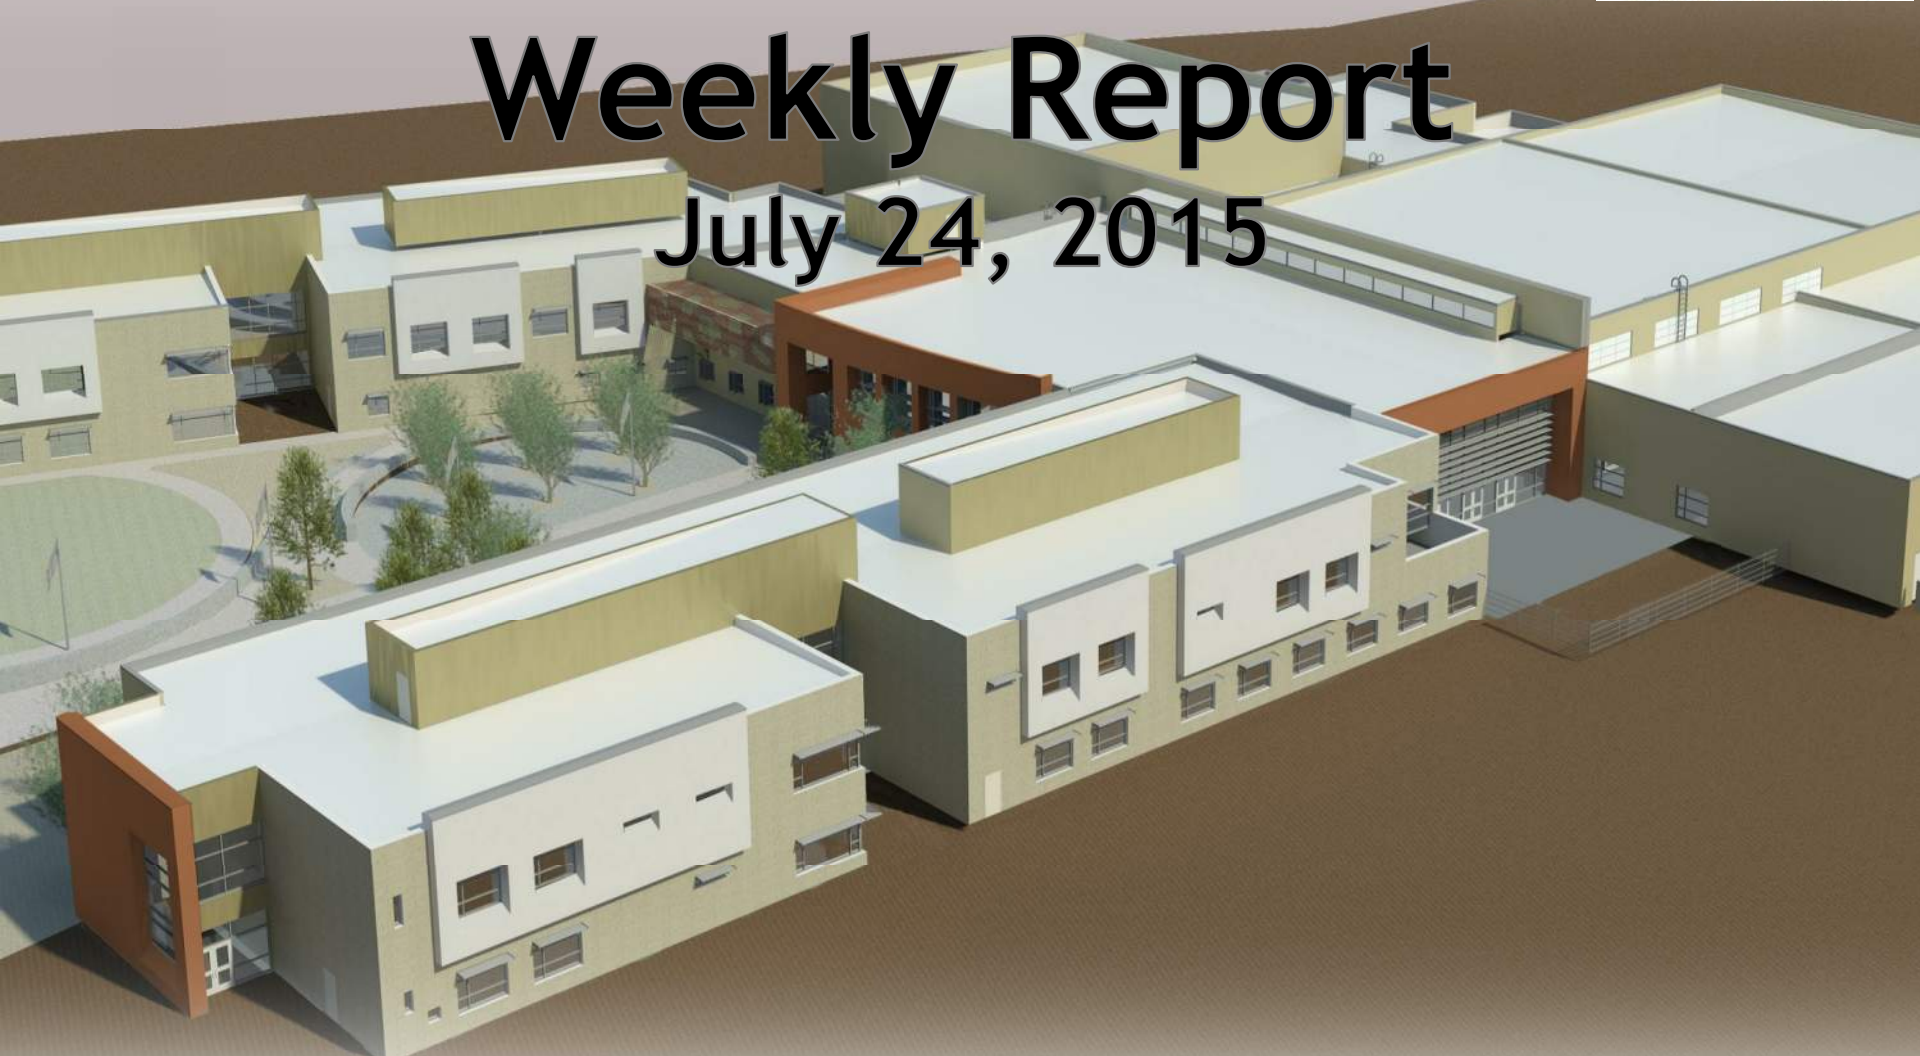

3-Week Look Ahead at Construction Schedule

- Work on Plaza modifications will be completed.
- Work on Multipurpose Field No. 2 will continue.
- Installation of irrigation system throughout the site will be completed. All landscaping, planting and native seeding will be completed.
- Mechanical, plumbing and electrical trimout will be completed.
- Testing , Adjusting and Balancing of Heat Pumps, ERV's and Roof Top Units will be completed.
- Functional testing and commissioning will be completed.
- Painting will be completed.
- Ceramic tile installation will be completed.
- Ceiling tile installation will be completed.
- Casework installation will be completed.
- Installation of marker boards, toilet partitions and toilet accessories will be completed.
- Installation of interior wood doors and hardware will be completed.
- Carpet and vinyl flooring will be completed throughout the building.
- Appliances will be installed.
- All interior and exterior signage will be completed.

Subcontractors On Site

- Advanced Concrete Solutions (site concrete/floor polishing)
- Advanced Contracting (toilet partitions and accessories)
- Ambassador Blind and Shutter
- American Fence Company
- Avalis Wayfinding
- Clark & Company (irrigation and landscaping)
- Cruzan Construction (rough carpentry, hollow metal doors & frames, wood doors)
- Denman Building Products (framing, insulation and drywall)
- Dynamic Fire Protection
- El Paso Flooring (hardwood gymnasium floor)
- Four Corners Materials (asphalt paving)
- Goff Engineering (surveying)
- Horizon Environmental Services (native seeding)
- HVAC Solutions & Garrhs Mechanical
- Nichols Electric
- OGB Architectural Millwork
- Reigles Mechanical (plumbing)
- Rio Grand Flooring (carpet, resilient vinyl flooring and wall tile)
- Stagecraft Industries (stage rigging)
- Summit Sealants (air barrier and joint sealants)
- Sun Glass (windows, aluminum store fronts and curtain walls)
- Topline Installers (roofing and metal siding)
- WBS Coatings
- W. West Equipment (food service)

Notable Onsite Activities This Week

- Continued installation of irrigation system and planting of trees and shrubs.
- Continued work on Multipurpose Field No. 2.
- Continued installing site furnishings.
- Continued paint touchup throughout the building.
- Continued flooring and tile installation in Areas C, F and G.
- Continued installation of door hardware throughout building.
- Continued installation of controls wiring in Areas C, F and G.
- Continued installation of access control and security systems hardware.
- Continued installation of plumbing fixtures in Areas C, F and G.
- Continued testing and balancing heat pumps and ERV's.
- Continued punchlist corrections throughout the building.
- Continued final cleaning in the building.
- Owner took occupancy of the Administration Area.
- Owner began moving furniture and equipment into the building from the existing high school.

Weekly Weather

20	Tstorm	21	Scattered Clouds	22	Scattered Clouds	23	Scattered Clouds	24	Rain
Actual: 86° 51°	Actual: 83° 51°	Actual: 88° 49°	Actual: 90° 51°	Actual: 84° 54°	0.06 in	0.00 in	0.00 in	0.00 in	T in
Average: 90° 54°	Average: 90° 54°	Average: 90° 54°	Average: 90° 55°	Average: 90° 55°	0.05 in	0.06 in	0.06 in	0.07 in	0.07 in

Multipurpose Field No. 1



07/25/2015 08:17

Multipurpose Field No. 2



07/25/2015 07:56



Student Drop-off Area

07/25/2015 07:58



Commons Banquet Seating

07/25/2015 08:28



Commons Stairs

07/25/2015 08:28
