


Project Overview

Program Wide Building Automation System

ARCHITECT: Whitaker & Rawson
 PROGRAM MANAGER: Hoar Program Management (HPM)
 CONTRACTOR: Alabama Controls, Inc.

SCOPE OVERVIEW:
 Bid Package #1
 Scope (May 2018-May 2019)
 New Enterprise Server System and Software, New Equipment Level Controllers at all schools and facilities to include All Elementary Schools, Middle School, High School, Waldrop Stadium, and Board of Education Office.

Example

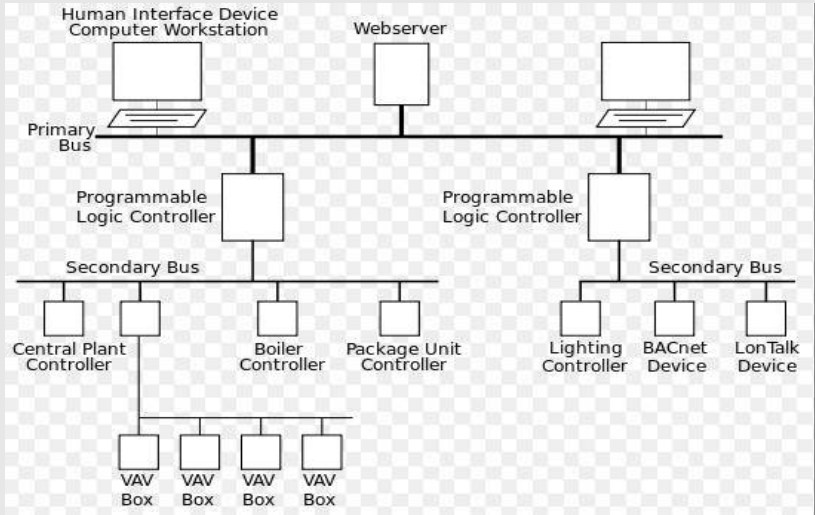

CONTRACT RECAP:	Projected Start	Executed CO	Projected Finish
• Contract Amount	\$1,132,000	TBD	TBD
• Contract Schedule	May 7, 18	TBD	February 4, 19

Construction Contract Amount:	Anticipated Completion Date:
\$1,132,000	02/04/2019

- ACHIEVEMENTS:**
- ✓ Bid
 - ✓ Bid Approval
 - ✓ Contract Execution
 - ✓ Pre-construction Conference
 - ✓ Issue Notice to Proceed
 - ✓ Start Construction
- Milestone Delivery Dates:**

- NEXT STEPS:**
- Complete Construction
- RISKS/URGENT NEEDS:**
- N/A

