



# Progress Report

**Client:** Wendell School District

**Facility:** Wendell High School

**Report Date:** 06/22/2017

**Roof Section:** Entire Roof

## Report Data

Title
Wendell High School Metal Roof

### Scope of Work

- Clean surface of all dirt, debris, existing paint or foreign materials
- Rinse and allow system to dry
- Prime & coat metal roof

### **Progress up to 6/22**

- June 7: Test section completed with coating (completed roof section thus far is approx. 2,000 square feet)
- June 7-14: Colorquest began media blasting the existing paint on the roof, starting from the east. Roof area that has been prepped is approx. 4,100 square feet
- June 14-22: As communicated earlier in the week, the compressor went down for Colorquest which has set us back a couple days. It will be back up and running this week (6/26- 6/30), as we know time permits.
- After all the existing paint from the roof is blasted off, Colorquest will begin coating the roof.



**Photo 1**

Field photo of completed section



**Photo 2**

Photo of wall flashing on the completed roof section




**Photo 3**

Continued- Up close




**Photo 4**

Completed section of roof edge

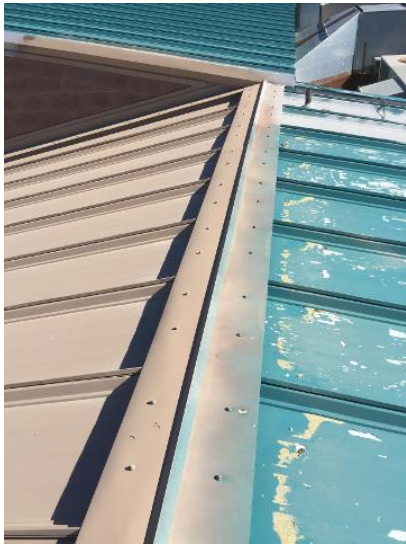

**Photo 5**

Photo of where the completed section ends at the ridge

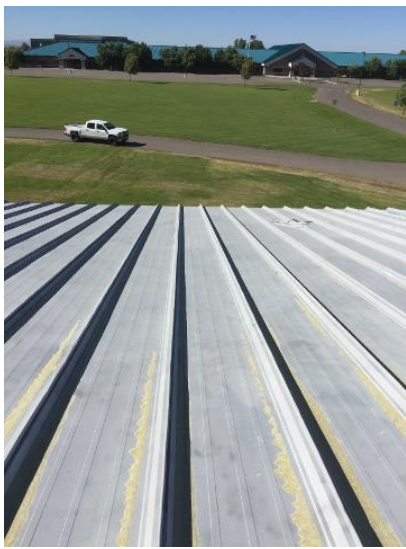

**Photo 6**

Field photo of prepped section



**Photo 7**

Continued



**Photo 8**

Continued- alternate angle



**Photo 9**

Prepped section of roof edge
